


## Notification of Survey and Soils Drilling

Issued February 8, 2016

Survey and soils investigations for the South Side Pigeon Lake Wastewater Collection System will be commencing shortly. The work will be completed in two stages as shown below:

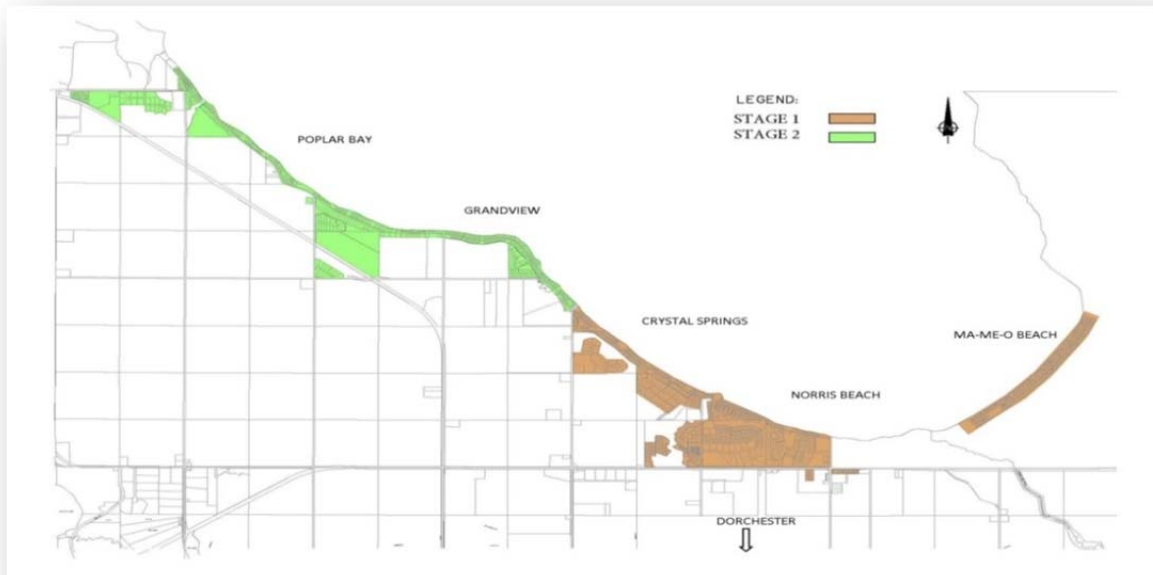

Utility locators (gas, Telus, etc.) will begin marking the utilities February 08, 2016 throughout Stage 1.

MPE Engineering will begin surveying Stage 1 and Stage 2 on February 09, 2016. The surveys will be throughout both stages, but predominately located in Stage 1. Some stakes will be left in the ground for soils drilling and future survey.

Parkland Geotechnical will begin the soils investigation February 15, 2016. Parkland Geo. will have a drill truck on site primarily drilling boreholes off the side of the road with some drilling on the road. Traffic will be reduced to one lane in these areas during drilling. A plastic white tube 25 mm in diameter will be left in the holes approximately 0.5 metres high outside of the roadway to monitor groundwater.

A tentative schedule for Stage 1 and 2 is listed below:

STAGE	ACTIVITY	SCHEDULE
1	Utility Location	Feb. 08 – Feb. 16
	Survey	Feb. 09 – Feb. 26
	Soils Drilling	Feb. 15 – Feb. 22
2	Utility Location	Feb. 22 – Feb. 29
	Survey	Feb. 16 – Mar. 31
	Soils Drilling	Feb. 29 – Mar. 07

Note: Limited work will be performed in Ma-Me-O Beach, as much of this work was completed last fall.

For any questions or concerns contact Gail at the Summer Village Office.
